

ARCHAEOLOGICAL MONITORING WORK PLAN FOR THE PROJECT BICYCLE AND PEDESTRIAN ROUTE FROM DOMES BEACH TO RINCÓN PUBLIC BEACH, RINCÓN [AC-500023]



Presented to:
Puerto Rico Highway and Transportation Authority

Prepared by:


Sharon Meléndez Ortiz, MA
Archaeologist

March 2018



CONTENT


I. Preamble	2
II. Project Background	4
Administrative Background	4
Archaeological Background	5
III. Project Description	9
IV. Archaeological Monitoring Procedure	13
A. Before construction begins	13
B. During construction	13
C. After construction ends	15
V. Summary of expected products	16
VI. Professional Qualifications	17
VII. References	18
Appendix 1	19



I. PREAMBLE

The Puerto Rico Department of Transportation and Public Works (DTPW), through its Highway and Transportation Authority (PRHTA) proposes the construction of a bicycle and pedestrian route in Rincón, Puerto Rico. The route, with an estimated length of 3.4 km, extends from Domes Beach at Punta Ward to Rincón Public Beach (Figure 1). It travels along a varied route which links the urbanized area with business district, employment centers, alternate transportation mode, schools, recreational facilities, cultural and environmental amenities, and the tourism district.

Figure 1: Project Location in Topographic Quadrangle (left) and Satellite Photo (right)

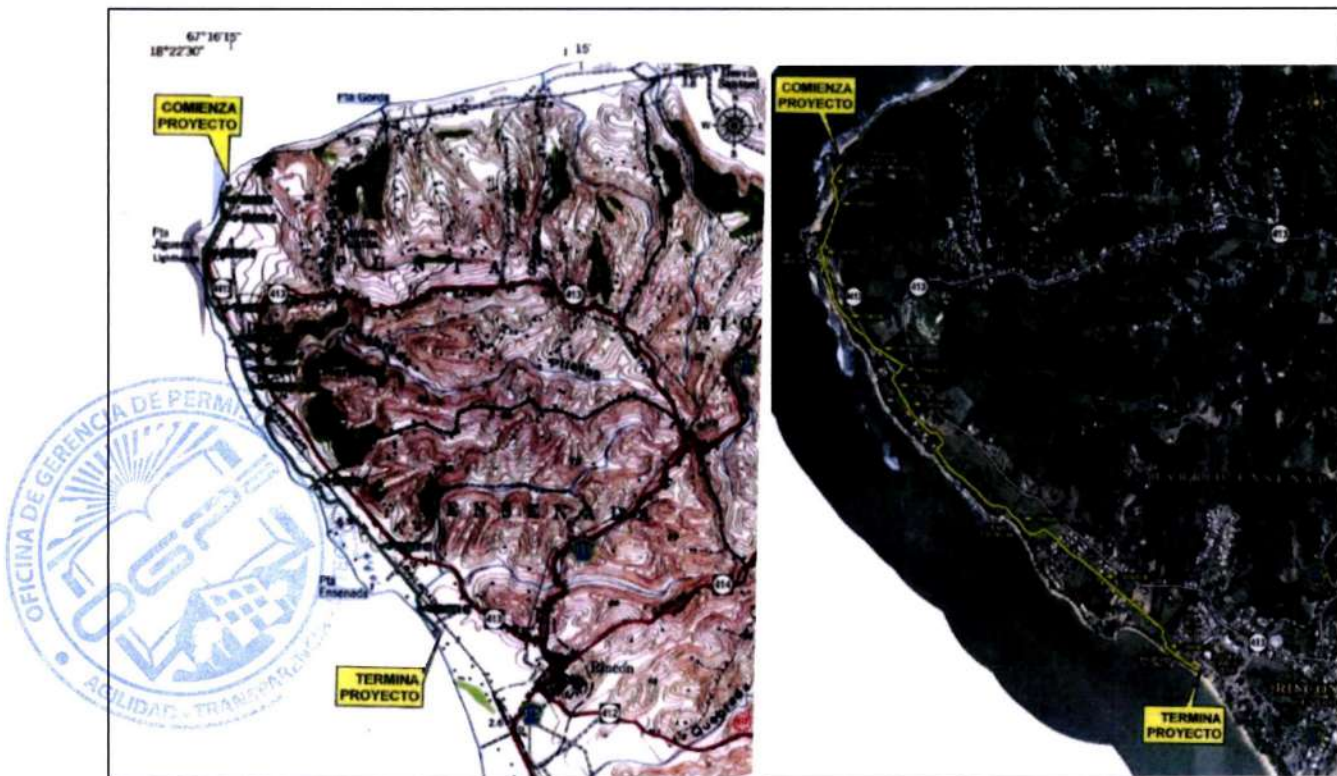

The bicycle and pedestrian route of Rincón will take its users near historical icons of the municipality, like the Lighthouse of Punta Higuero -listed in the National Register of Historic Places- and the old Nuclear Plant. In some sections, the trail will run on the old route of the *Tren de Circunvalación*, passing through paths cut in stone, and over historical culverts. The trail will also pass very close to a pre-Columbian site, Punta Ensenada, the most important known so far in the area, still hidden under layers of dirt.

Due to the historic importance of this area, the State Historic Preservation Office (SHPO) and the Archaeology and Ethnohistory Program (PAE by its Spanish acronym) of the Institute of Puerto Rican Culture (IPRC) requested an archaeological monitoring of the project's construction activities. This document constitutes the work plan for such monitoring.

DEC 16 2025

This plan complies with all federal and state applicable laws, regulations and guidelines, especially the *Reglamento para la radicación y evaluación arqueológica de proyectos de construcción y desarrollo* (Regulation #8932 of February 8, 2017) of the Council for the Protection of the Archaeological Terrestrial Heritage of Puerto Rico (Council), ascribed to the IPRC, and it is consistent with the *Standards and Guidelines for Evaluation and Archeological Documentation*, the *Standards and Guidelines for Archaeology and Historic Preservation*, and the *Standards and Guidelines for Architectural and Engineering Documentation* of the U.S. Secretary of the Interior, and the National Park Service Bulletins *How to Apply the National Register Criteria for Evaluation* (Secretary of the Interior 1990) and *Guidelines for Evaluating and Registering Archeological Properties* (Little et. Al 2000). The plan was prepared by archaeologist Sharon Meléndez Ortiz, whom meets the Professional Qualifications Standards set forth at 36CFR Part 61.

This work plan is divided into seven (7) sections. After this preamble, the Project administrative and archaeological background is discussed. This section is important to understand the project's changes and modifications along more than 15 years of administrative history. The third section includes a detailed description of the project, emphasizing those construction activities that will require archaeological monitoring. The archaeological monitoring procedure is discussed in the fourth section, while a summary of the expected products is included in the fifth section. In section VI the professional qualifications of the principal investigator are discussed, while in the last section the references cited are listed.






II. PROJECT BACKGROUND

Administrative Background

The Projected Bicycle and Pedestrian Route of Rincón has been in development for more than fifteen years. As expected, it has undergone significant changes since 2003, when the consultation process with the SHPO and the PAE/IPRC began. The initial phase of the project took place between 2003 and 2009. Problems with the identification of funds delayed the development, until 2016, when the PRHTA decided to continue with its design and construction. The agencies that had participated in the previous process were consulted again.

Originally, the Project had a length of 6.6 km, almost twice than in the present. It extended from PR-15, near the Treatment and Diagnostic Center, to PR-4413 interior. For construction purposes, the project was divided into two phases: Phase I extended from the Rincón Public Beach up to the Nuclear Plant; and the Phase II extended from the Nuclear Plant up to the west of Punta Gorda (Figure 2). As part of the modifications to the original concept of the project, the second phase was eliminated due to significant environmental changes that occurred in this segment after 2009. Severe erosion along the northern coast of Rincón required the realignment of the trail which ran along the old railroad route. The realignment would require the acquisition of properties, increasing substantially the cost of the project.

Figure 2: Original Project Extension

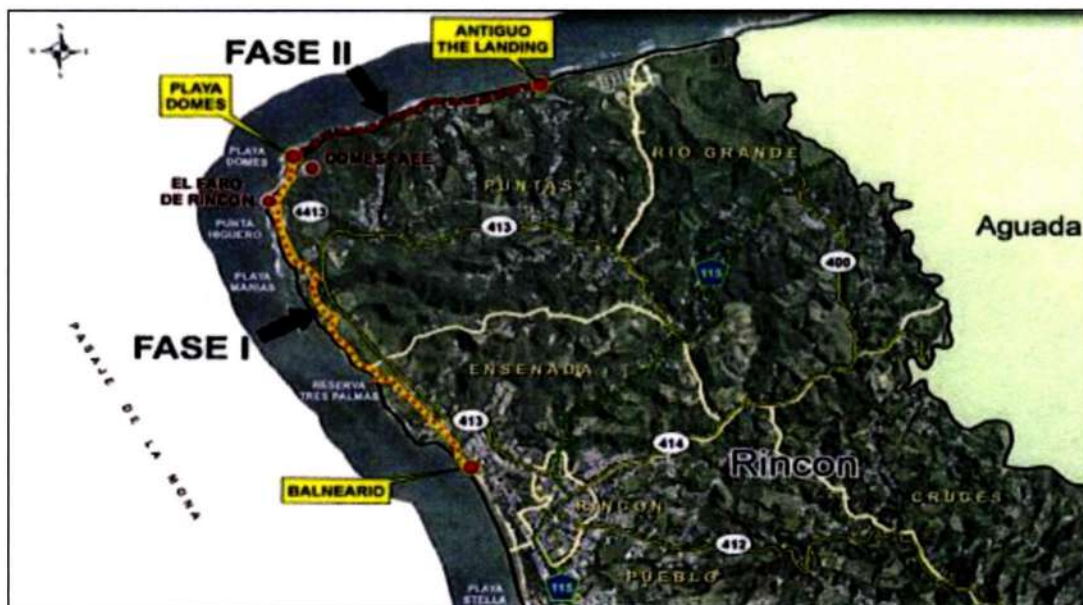

The project suffered additional changes after 2016. The modifications included: the use of the existing trails in Playa Las Marías, instead of the proposed route which impacted dunes and areas with vegetation between the beach and the existing road; widening of road PR-4413; widening of Camino Los Velázquez; and the construction of a wall to control coastal erosion along the limit of the property adjacent to the Public Beach.

The last change occurred in 2017, when the access to Step Beach was modified. A new entrance to the beach is proposed, eliminating the current access -which floods during rain events. This change entails the installation of a 30"-diameter reinforced concrete pipe. Because the installation of the pipe requires the removal of a white mangrove tree, 15 new white mangrove trees, between 4 to 6 feet height, will be planted. Also, the existing fill material deposited among the trees adjacent to the existing road will be removed, and a 111 m-long ornamental fence will be installed around the new trees and wetland.

The project area was visited by PRHTA personnel in January 2018 with the purpose of evaluating any changes due to Hurricanes Irma and María. No significant changes were identified, and the project may continue as planned.

Archaeological Background


The first archaeological study for this project was conducted by Miguel Rodríguez López in 2003. The Phase IA-IB archaeological assessment covered the original project area, as depicted in Figure 2. Rodríguez divided the project route into six (6) segments, identified with the letters A to F. He conducted a pedestrian survey along the six segments and excavated 72 manual test pits in areas with high archaeological sensitivity, all with negative results.

Nine (9) cultural resources were identified along the original project route (Figure 3). These are, from north to south: 1) brick and stone masonry culvert under the road to Punta Gorda; 2) historic culvert of the Punta Gorda Canal; 3) stone path of Punta Gorda; 4) Nuclear Plant; 5) Punta Higuero Lighthouse; 6) historic culvert on Leticia Creek; 7) brick and stone masonry culvert on Ensenada Creek; 8) pre-Columbian site Punta Ensenada (R-1); and 9) Cambija of the old railroad (Rodríguez López 2003: 8). The four (4) historic culverts, stone path and water reservoir (cambija) are associated with the Tren de Circunvalación, operated by the American Railroad Company of Puerto Rico during the first half of the 20th century.

The only pre-Columbian site identified in or near the project area is Punta Ensenada, an important archaeological site that has yielded evidence of occupation from the Saladoid to the Chican Ostionoid



Figure 3: Location of Cultural Resources in the 2003 Archaeological Survey (reproduced from Rodríguez López 2003)

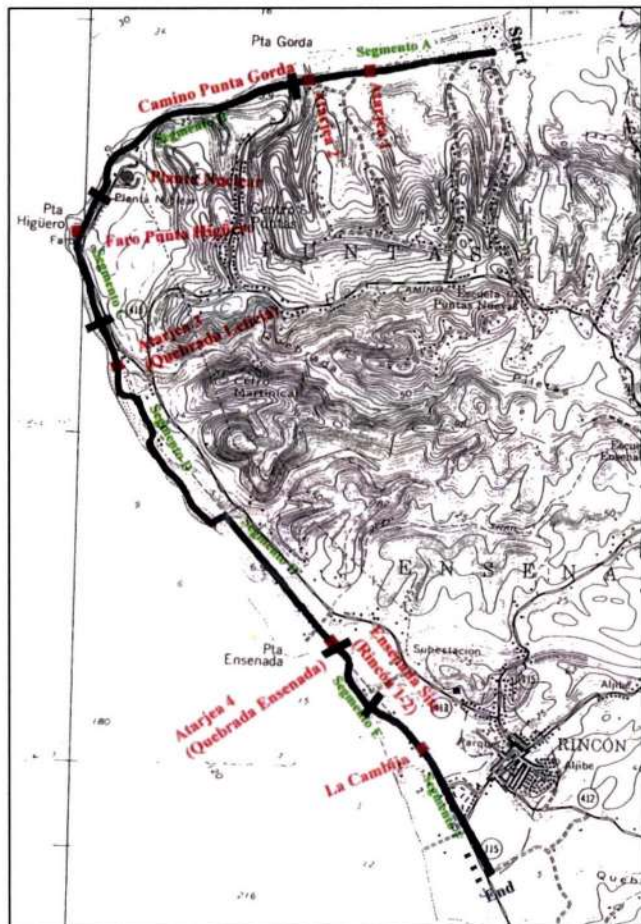

periods. The site is located near the Rincón Public Beach, along the limits of Alfredo Caro's property, and parallel to the coast. In 2003, Rodríguez López did not obtain access to survey segment E, precisely where the archaeological site is located.


The 2003 archaeological report did not recommend additional studies, except for the Punta Ensenada site area (Segment E), where a Phase IB survey was recommended. This survey was conducted one year later (see below). Rodríguez López proposed the incorporation of the properties into the trail by means of signs and the preparation of an informative document with a brief historical synopsis (Rodríguez López 2003: 20).

After evaluating the 2003 Phase IA study, on a letter dated October 16, 2003, the PAE/IPRC requested a Phase II Evaluation of the Punta Ensenada area and a description and documentation of the historic structures located along the project route. This study was not carried out, as will be discussed below.

The Phase IB of Segment E was conducted on March 2004 by Miguel Rodríguez López. The archaeologist excavated 18 manual test pits at 10 and 20 m intervals. Eight (8) test pits resulted positive to precolonial and colonial artifacts. The precolonial artifacts consisted of very small ceramic sherds, without diagnostic traits. The colonial artifacts also consisted of small sherds of utilitarian non-diagnostic pottery. Because the recovered pottery fragments were scattered and mixed between layers of fill, Rodríguez López concluded that they were not in a primary context, and as thus did not recommended additional studies. He concluded that the bulk of Punta Ensenada archaeological site is concentrated east of the Caro family property, close to the limit with the Vista Azul development.

Due to the results of the underground testing of Segment E, the PRHTA requested the elimination of the 2003 PAE/IPRC Phase II requirement. The Council for the Protection of the Archaeological Terrestrial Heritage (The Council), on a letter dated from July 28, 2004, granted the PRHTA petition. Instead, the Council required an archaeological supervision of the area near the archaeological site. On the other hand, the SHPO, on a letter dated June 25, 2004, commented that *"given the level of development of this specific project, which we understand as minimal, since the bicycle path will not affect much lower subsurface levels, and given the results of the work presented in the Report submitted [Rodríguez's 2004 Phase IB survey], the possibility of impacting a historic property (be it archaeological or historic) is minimal. Consequently, our records support your finding that no historic properties are located within the project's area of potential effects"*.

In 2008, three (3) segments of the proposed trail were realigned, moving east, away from the coast. Archaeologist Jaqueline López Meléndez conducted a Phase IB subsurface survey of these areas. López Meléndez labelled the segments Areas A, B and C (Figure 4). It must be stressed that these areas do not correspond to Miguel Rodríguez's A, B and C segments. López Meléndez Areas A and B are located within the limits of Rodríguez López segment D; and Area C is within Rodríguez's segment E.



Archaeological Monitoring Work Plan for the Bicycle and Pedestrian Route of Rincón.


Certifico que esta copia es fiel y exacta del documento original y para que así conste, firmo la presente en San Juan, Puerto Rico hoy, **DEC 16 2025**

-7-

In Area A, López Meléndez excavated 8 manual test pits at a 40 m interval, all negative to archaeological artifacts. One historic culvert is in this area. Nineteen (19) test pits, also at a 40 m interval, were excavated in Area B. Artifacts were found in two (2) of them: a small brick fragment in Test Pit B-12, and a fragment of coarse earthenware and a fragment of clear glass in B-14. In Area C, 14 test pits were excavated at 20 m intervals. Five (5) test pits resulted positive; three (3) to glass fragments (C-4, C-6 and C-11), and three (3) to brick fragments (C-6, C-8 and C-9). No pre-Columbian remains were identified.

López Meléndez recommended that an archaeological monitoring be carried out in Area B, where the coarse earthenware sherd was identified. She also recommended an archaeological supervision for the area near archaeological site R-1 or Punta Ensenada. This area was mistakenly identified in her report as Area A, instead of Area C. This typo was reproduced in later correspondence with the regulatory agencies. Bottomline, López Meléndez recommended an archaeological monitoring for Areas B and C (Figures 4 and 5).

Figure 4: Location of Areas A, B and C in the 2006 Archaeological Study (reproduced from López Meléndez 2008)

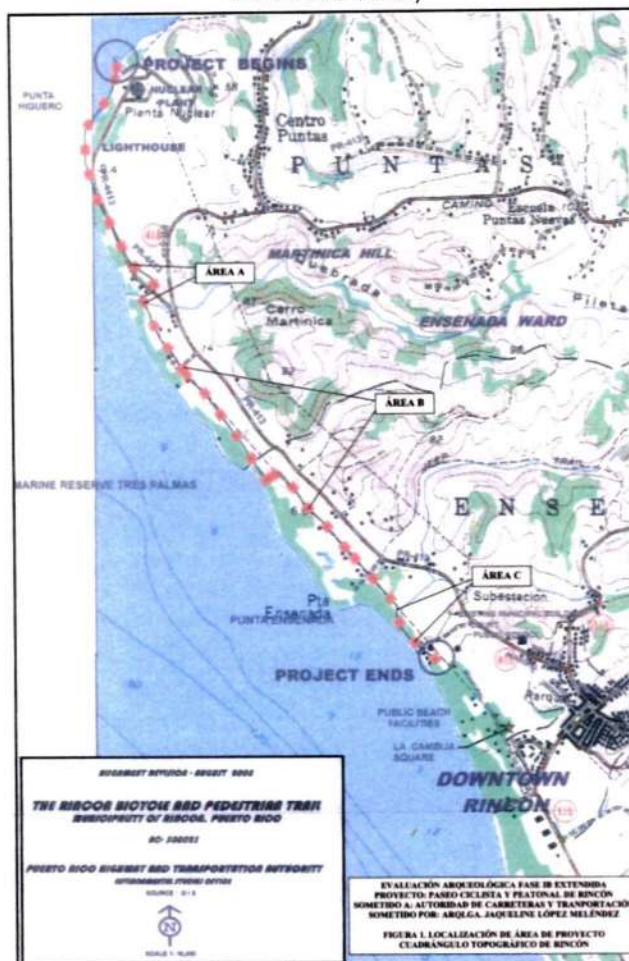

The SHPO, on a letter dated November 7, 2008, agreed that a determination of no historic properties affected is adequate for the project, conditioned to the implementation of an archaeological monitoring in areas B and C¹. The agency requested that an archaeological monitoring work plan be submitted for their review and concurrence. The Council, on letter dated 20 November 2008, authorized the project, conditioned to an archaeological supervision of areas B and C², and the preparation of a preservation plan for the historic box culvert located in area A.


The Preservation plan for the historic box culvert was prepared and submitted to the Council in 2009 by the late Cultural Heritage Office of the PRHTA. The plan included the following actions: 1) Removal of trees, plants and fungal growths from wall surfaces and the immediate perimeter of the structure; 2) Removal of loose and detached surface material; 3) Cleaning of all exposed surfaces; 4) Cracks, voids are

¹ The letter says Area A instead of C. As was explained before, this is due to a typo in López Meléndez archaeological report.

² Same as above.

to be filled and missing elements replaced; and 5) Finishing joints to achieve desired aesthetic appearance (to be specified by the PRHTA).

Figure 5: Location of Areas B and C in Satellite Image (from López Meléndez 2008)

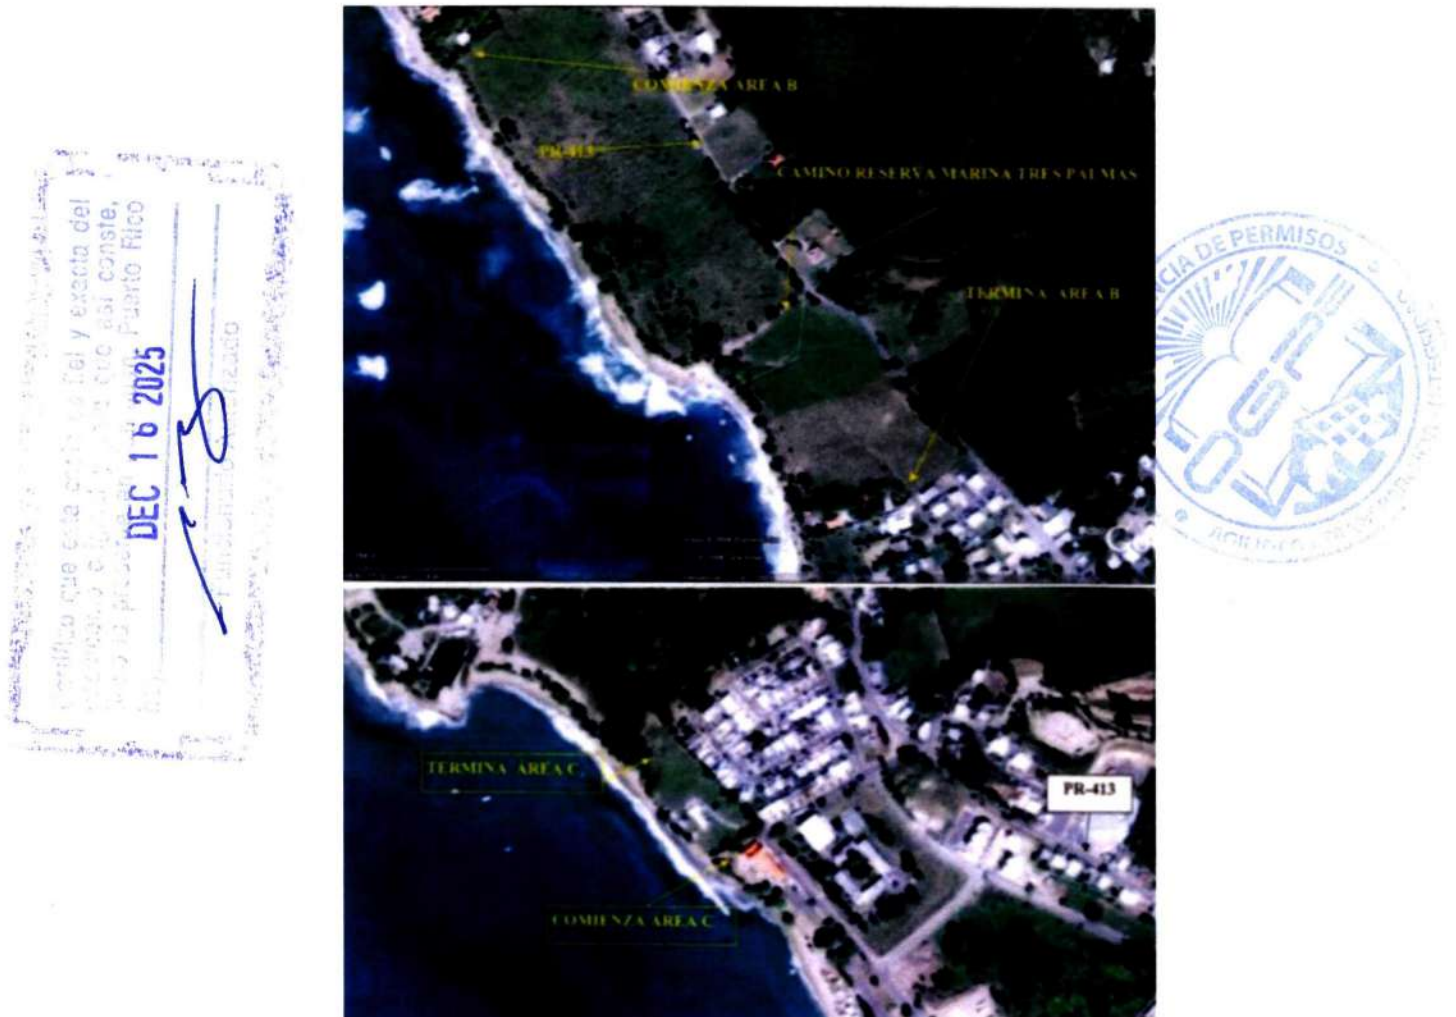

After 7 years of inactivity, in 2016, the PRHTA resumed the project's consultation process. As was discussed above, now the project included only the southern portion of the original route, decreasing its extension to approximately 3.4 km. New consultation letters were sent to the SHPO and PAE/IPRC, summarizing the project changes. The PAE/IPRC, on a letter dated June 1, 2016, authorized the new project, conditioned to an archaeological supervision of the project's construction activities that entail demolition, excavations or earth movements. For its part, the SHPO requested additional information, specifically location on USGS Topographic Quadrangle; boundaries of the area of potential effect (APE); current photos; and a set of scale drawings depicting all identification efforts from previous surveys within the APE. Finally, on a letter dated August 19, 2017, and after reviewing the additional information highlighting the changes made to the project, the SHPO reiterated their request from November 2008 for the development and implementation of an archaeological monitoring work plan.



9-
DEC 16 2025

III. PROJECT DESCRIPTION

The Project Bicycle and Pedestrian Route of Rincón consists of the construction of a 3.4 km long, ca. 3.65m wide bicycle and pedestrian route along the coast. The route runs over existing sand trails, dirt paths, the old railway path, and paved roads, with three segments crossing vacant areas. To facilitate its description, the PRHTA divided the project into 11 sections [refer to Appendix 1], as follows:

Section 1-Pedestrian Trail

This section -210 m long- consists of a pedestrian path that will use the existing sand trails. It begins at Domes Beach, with a typical section 2 m wide with concrete curbs in both sides and paved with sand from the same beach.

Section 2 – PR-4413, from the old nuclear plant parking to Rincón Lighthouse

This segment -3.65 m wide-extends 200 m along PR-4413. The trail will be separated from the automobile lanes by bollards, and it will have guardrails on the other side. The westbound side of PR-4413 will be widened.

Section 3- The Lighthouse

The route crosses 150 m in front (east) of the Lighthouse, over its parking area, until connecting with a dirt path. The 3.65 m-wide trail will be paved with concrete. The lighthouse parking area will not be affected.

Section 4- Dirt path in front of Las Marías Beach

This section extends 380 m parallel to PR-4413, but to the west, near the beach, until intersecting again the PR-4413. It entails the construction of concrete curb and gutters; the installation of drainage pipes; and the construction of a concrete gravity wall.

Section 5- Along PR-4413, in front of Calypso

For the next 210 m, the route will continue along PR-4413. Concrete curbs will be constructed in both sides of the trail.

Section 6-From PR-4413 to the Old Railway

At the end of section 5, the route turns west, perpendicular to PR-4413, 85 m cross country until connecting with the old railway path. Concrete culverts will be built at both sides of the trail.

Section 7- Old Railway Path

For the next 155 m, the route will use the old railway path, until connecting with Camino Los Velázquez. There is one historic culvert located in this segment. Over it, ornamental guardrails will be installed. Also, a retaining wall will be built, and galvanized wire fences will be installed.

Section 8- Caminos Los Velázquez

The route continues 175 m along a paved segment of Camino Los Velázquez. The pavement, 3 to 5 m wide, will be covered with a bituminous mixture. At the end of the section, the project will intercept a municipal road that in turn connects with PR-413.

Section 9- Cross-country and access to Step Beach

The next 915 m runs along a vacant area covered with vegetation. Along this section, concrete curbs and drainage pipes will be constructed. In the first 80 m, ornamental guardrails will be installed. It is proposed to construct a circular intersection where the trail connects with the access road to Step Beach. Because this area is floodable, it is proposed to install a drainage structure consisting of a reinforced concrete pipe 30 inches in diameter and 7.67 m long. It is also proposed to remove the fill material that is at the end of the road, to give continuity to the storm drainage area. The installation of the drainage structure involves the removal of a white mangrove tree. To mitigate this removal, the planting of 15 white mangrove trees and the removal of the material that has been placed as a fill inside the adjacent grove was proposed. A wooden ornamental safety fence will be installed around the newly planted trees and part of the wetland.


Section 10-Camino José Pérez

This road is 430 m long, with a variable width of 3 to 5 m. Concrete curbs will be built in both sides, and the surface will be paved with a bituminous mix.

Section 11-Cross-country to Rincón Public Beach

The last 498 m of the trail runs through pastures, groves and recreative areas. There is a second historic culvert in this section. This segment entails the construction of culverts, drainage pipes, a 100 m-long retaining wall, and the demolition of a 110m-long existing wall. Construction of a Polymeric Circular Cell System that would behave like a retaining wall and a coastal erosion control system, 100 m long and 1.33 m height (from station 32+25 to 33+25). The existing wall, which is partially collapsed, will be demolished and the debris and vegetation found in the coastal strip will be removed to provide more coastal area. Archaeological site R-1 is located in or adjacent to this section.

In summary, the project involves -as a minimum- the following construction activities: construction of concrete curbs and gutters at both side of the lane; paving of the route's surface; installation of several drainage structures, like pipes, inlets, culverts and manholes; construction of several gravity or retaining walls; installation of bollards, ornamental barriers, trellis and safety barriers; removal and sowing of trees; installation of new lighting; and relocation of utilities, like PREPA, PRASA and PRTVO.



The next table summarizes the cultural resources known per section of the project. The location of the sites is depicted in the figures included in appendix 1, and photos of some of the resources are included in the page that follows.

Table 1: Brief description of cultural resources within or adjacent the project area

Cultural Resource	Description	Section
Lighthouse Punta Higuero	Also known as Rincón Lighthouse. It was built in 1892, but it was partially destroyed during the 1898 earthquake. It was reconstructed in 1921. Listed in the National Register of Historic Places.	3
Railroad path	Right of way of the <i>Tren de Circunvalación</i> . It has segments cut in stone. Constructed ca. 1893.	7
Historic culvert #1	Arched box culvert, constructed in stone and brick masonry. Associated to the <i>Tren de Circunvalación</i> . Constructed ca. 1893.	7
Area of Interest #1 (Aol-1)	Area (test pit B-14) where López Meléndez identified a potential pre-Columbian earthenware sherd.	9
Path cut in stone	Path cut in the stone (at Calle José Pérez).	10
Historic culvert #2	Arched box culvert, constructed in stone and brick masonry. Associated to the <i>Tren de Circunvalación</i> . Constructed ca. 1893.	11
Archaeological site R-1	The site Punta Ensenada consists of shell mounds, with fragments of Saladoid, Ostionan and Chican Ostionoid ceramics. Partially excavated by Ovidio Dávila in 1978.	11





Photo 1: General views of some of the cultural resources present in the project's area



1: Punta Higuero Lighthouse; 2: Historic culvert #1; 3: Area of Interest #1 and sample of the course earthenware found in test pit B-12; 4: Area where part of archaeological site R-1 is located; 5: General view of path cut in stone; 6: Detail of cut stone at José Pérez Street.





DEC 16 2025

-13-

IV. ARCHAEOLOGICAL MONITORING PROCEDURE

The SHPO and the IPRC required the implementation of an archaeological monitoring plan for this project. The monitoring has two (2) main objectives: (1) to ensure that the cultural resources that are located within or adjacent to the project area are not adversely affected by or during construction activities; and (2) to identify and evaluate any previously unidentified resources discovered after the construction of the project has commenced.

The monitoring activities can be divided into three groups: those to be carried out before the project begins, those to be carried out during the project's construction activities, and those to be performed after the construction activities that need to be monitored are concluded. Only those activities that entails excavations or earth movements shall be monitored. Also, all activities conducted in areas with cultural resources, specifically in the two historic culverts and in the old train path, shall be monitored, regardless of the type of construction activity.

A. Before construction begins

A-1. The PAE/IPRC and SHPO must be notified of the construction start date and of the archaeologist who will oversee the monitoring before construction activities begin.

A-2 The construction crew, inspectors and archaeologist will have a kickoff meeting, where the procedure to be carried out during the archaeological monitoring will be discussed, including the coordination protocol between the archaeologist and the contractor. The archaeologist will provide an orientation on the cultural resources of the area, and on the proper treatment to them. The archaeologist will also explain which construction activities require archaeological monitoring.

A-3 The archaeologist must photographically document the state of the cultural resources found in the project area before construction begins. These photos shall be included in the first weekly report.

B. During construction

B-1. A qualified archaeologist (refer to section VI) will be in the field whenever there are construction activities that require excavation or earth movements, or when working in or in the immediate environs of known cultural resources (refer to Table 1). ***No excavations or earth movements shall be carried out without the presence of the qualified archaeologist.***

B-2. The Archeologist will provide instructions directly to the Contractor's field personnel as to how to proceed when she understands that there is a potential to impact an archaeological resource. The Contractor's field personnel should abide to the requests of the archaeologist: excavate slowly, stop the excavation work to evaluate a finding, etc.

B-3. The monitoring process shall be conducted in close coordination between the PRHTA inspectors, the contractor and the archaeologist.

B-4. The monitoring activities in or in the immediate environs of known cultural resources shall ensure that any hidden or previously unseen features of the resources are documented, including unknown details about their components, material and method of construction.

B-5. Any unanticipated archaeological remains (artifacts, structure, features, etc.) found during construction activities shall be identified, evaluated and if significant, documented. The archaeologist will instruct that activity in the area cease immediately. This interruption will be temporary until the remains are exposed and a preliminary evaluation is made in order to determine the nature of the finding, artifact content, possible cultural association, degree of integrity and extension. The excavation will be halted while the archeologist makes this determination. It is possible that, to complete this evaluation, the archeologist will need the support of the contractor and additional personnel from the archeological team.

If the findings are considered exceptional - like human burials, complex structures, and stratified archaeological deposits- the archaeologist must prepare a statement of significance and shall notify -via email and text message- the PRHTA's inspector within 24 hours of the discovery. The PRHTA's inspector shall then notify the PAE/IPRC and the SHPO within 48 hours of the discovery. The statement of significance shall include a description of the finding, an explanation of why it is considered significant, and recommendations on steps to follow for proper resource documentation. If deemed necessary, additional staff may be mobilized to document the resource. The documentation will be done within a reasonable amount of time, trying as much as possible not to impact the project schedule. The documentation of exceptional findings may require the preparation of a technical proposal that shall be reviewed and approved by the regulatory agencies before its implementation.

B-6. During periods of no excavation or earth movements, the archaeologist shall visit the project once a week to ensure that the cultural resources located within the project area have not been adversely affected.

B-7. The monitoring process and weekly visits will be documented by means of written descriptions, photographs, and drawings, if necessary. The archaeologist shall keep a field diary with a record of the activities carried out, location of archaeological finds, presence of archaeological materials and structural elements and general stratigraphy, as a minimum.

B-8. The archaeologist shall submit weekly reports to the PRHTA, describing the activities supervised and the findings, if any. The weekly reports shall include photographs of the activities being monitored and of the cultural resources present in the area. The report will be sent via email during the week that follows. The PRHTA will be responsible to submit the reports weekly to the SHPO, and monthly to the PAE/IPRC.

B-9. The processing of archaeological artifacts, if any, shall be carried out simultaneously with the field work. The artifacts will be washed, classified, analyzed and graphically documented. If necessary, a documentary research will be performed for the analysis and interpretation of the findings. A summary of these activities shall be included in the weekly report.



DEC 16 2025

C. After construction ends

C-1. The PAE/IPRC and the SHPO shall be notified when the construction activities are completed. In said communication, the estimated delivery date of the final report shall be indicated.

C-2. A technical report shall be prepared detailing construction activities that were monitored, documentary research, documentation of findings, analysis and interpretation of the results. It shall include graphic information, such as drawings and photos, as well as a sketch plan of all the documented findings. A digital copy of the draft report shall be submitted to the PRHTA for comments no more than 60 calendar days after the undertaking is completed. The PRHTA shall forward the report to the FHWA, for review and comment. After acceptance by all parties, three (3) hard copies of the report (hard and digital) will be submitted to the PRHTA no more than 10 calendar days after the comments on the draft report are received.

DEC 16 2025




V. SUMMARY OF EXPECTED PRODUCTS

The expected products are the following:

- Weekly reports, to be submitted within the following week. These reports will be submitted via email to the PRHTA. The PRHTA shall be responsible of forwarding the report to the SHPO weekly and to the PAE/IPRC monthly. The report shall summarize the monitoring activities that took place during the week, it shall describe unexpected and documented remains, if any; and it shall include photographs and drawings if deemed necessary.
- Draft monitoring report. A digital copy of the draft report shall be submitted to the PRHTA for comments no more than 60 calendar days after the undertaking is completed. The PRHTA shall forward the report to the FHWA for review and comments.
- Final monitoring report (hard and digital in .PDF). This report shall include the FHWA and PRHTA comments, if any. Three (3) hard and digital copies shall be submitted to the PRHTA no more than 10 calendar days after the comments on the draft report are received.

Table 2 summarizing expected products, date of delivery, format and number of copies

Product	Date of delivery	Format/# of Copies
Weekly reports	The next week to the PRHTA. The PRHTA shall delivered them weekly to the SHPO; and ten (10) days of the last calendar day of the month to the PAE/IPRC.	Digital /Email
Draft monitoring report	To be submitted to the PRHTA and FHTA for comments, no more than 60 calendar days after the undertaking is completed.	Digital /Email
Final monitoring report	To be submitted to the PRHTA no more than 10 calendar days after the comments on the draft report are received.	3 printed copies; 3 CD/DVD with a digital copy in .PDF.




VI. PROFESSIONAL QUALIFICATIONS

An archaeologist listed in the Council's list for Phase II -and preferably Phase III- will serve as principal investigator and shall be on the field always during fieldwork. The archaeologist shall meet at a minimum the Professional Qualifications Standards set forth at 36CFR Part 61. These are: a graduate degree in archaeology, anthropology, or closely related field, plus at least one (1) year of full-time professional experience or equivalent specialized training in archaeological research, administration or management; at least four (4) months of supervised field and analytic experience in general Puerto Rican archaeology; the demonstrated ability to carry research to completion; and at least one (1) year of full-time professional experience at a supervisory level in the study of archaeological resources of the pre-Columbian and colonial periods.

Any additional personnel to intervene in the monitoring efforts shall have vast experience in pre-Columbian and historical archaeology, and in working in evaluation (Phase II), documentation (Phase III), and monitoring projects dealing with properties of the precolonial and colonial periods.

The archaeologist shall not defer his or her monitoring responsibilities to any crew member that does not meet the professional qualifications for archaeology.



VII. REFERENCES

Advisory Council on Historic Preservation

1980 *Treatment of Archeological Properties: A Handbook*. http://libraryarchives.metro.net/DPGTL/archaeology/1980_treatment_archaeological_properties.pdf

Consejo para la Protección del Patrimonio Arqueológico Terrestre de Puerto Rico.

2017 *Reglamento para la radicación y evaluación arqueológica de proyectos de construcción y desarrollo*. San Juan: ICP. Reglamento #8932 del 8 de febrero de 2017.

López Meléndez, Jaqueline

2008 *Evaluación arqueológica fase IB extendida, Proyecto: Paseo ciclista y peatonal de Rincón, Puerto Rico*.

National Park Service

s/f "Archeology and Historic Preservation: Secretary of the Interior's Standards and Guidelines [As Amended and Annotated] Professional Qualification Standards". https://www.nps.gov/history/local-law/arch_stnds_9.htm

s/f "Archeology and Historic Preservation: Secretary of the Interior's Standards and Guidelines for Archeological Documentation". http://www.cr.nps.gov/local-law/arch_stnds_7.htm [consultado feb. 2013]

s/f "Archeology and Historic Preservation: Secretary of the Interior's Standards and Guidelines for Historical Documentation". http://www.cr.nps.gov/local-law/arch_stnds_5.htm

s/f "Archeology and Historic Preservation: Secretary of the Interior's Standards and Guidelines for Identification". http://www.cr.nps.gov/local-law/arch_stnds_5.htm

Puerto Rico State Historic Preservation Office (PRSHPO)

1993 *Guía para hacer investigaciones arqueológicas Fases I, II y III*. San Juan: Oficina del Gobernador.

Rodríguez López, Miguel

2003 Estudio Arqueológico Fases 1A-1B Proyecto Paseo Escénico y Ciclista de Rincón (The Rincon Bicycle and Pedestrian Trail").

2004 Estudio Arqueológico 1B, Segmento E, Paseo Escénico y Ciclista de Rincón.

